


BRHAT BANGALORE MAHANAGARA PALIKE
INSPECTION REPORT

SI No	Decription	Details	Remarks
1	Name of Work	Improvements to Road and Drains at Ambedakar Colony Left Side Layout in Ward No 06 Thanisandra Village Limit	
2	Estimate Cost	60.0 lakhs	
3	Administrative Approved No and Date	568/13-14, Date. 23.12.2013	
4	Technical sanction No. and Date	196/13-14, date. 23.12.2013	
5	Job Code No. and P Code No.	006-14-Q00079	
6	Tender Direct Entrested to KRIDL	KRIDL	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applicable	
8	Tender Approved Details	Not Applicable	
9	Work Order No and Date	425/2013-14, Date. 21.02.2014	
10	Stipulation time of Completion	90 Days	
11	Actiual Date of Commencement	30.07.2014	
12	Actiual Date of Completion	28.08.2014	
13	Delay if any	Nil	


	Reson for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verified	Enclosed	
18	Date of Inspection	02.07.2014	
19	MB No. and Page No.	Mb No. 2561/14-15 Page No.256001-13	
20	BR No and Date	334/30.08.2015 ²⁰¹⁴	
21	Test Result	Quality Test Report submitted by Bangalore University is verified and Enclosed	
22	Section officer	Sri K Devegowda JE	
23	Sub Division Officer	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
A	Work Quality	Satisfactroy	
B	Comments	Work completed as per MB	

Samir
Executive Engineer
Byatarayanapura Division
Yalahanka Zone, B.B.M.P.
Bangalore-560092

Y. C. Kale 2/7/15
Y C Kale gowda
Executive Engineer (Retd)

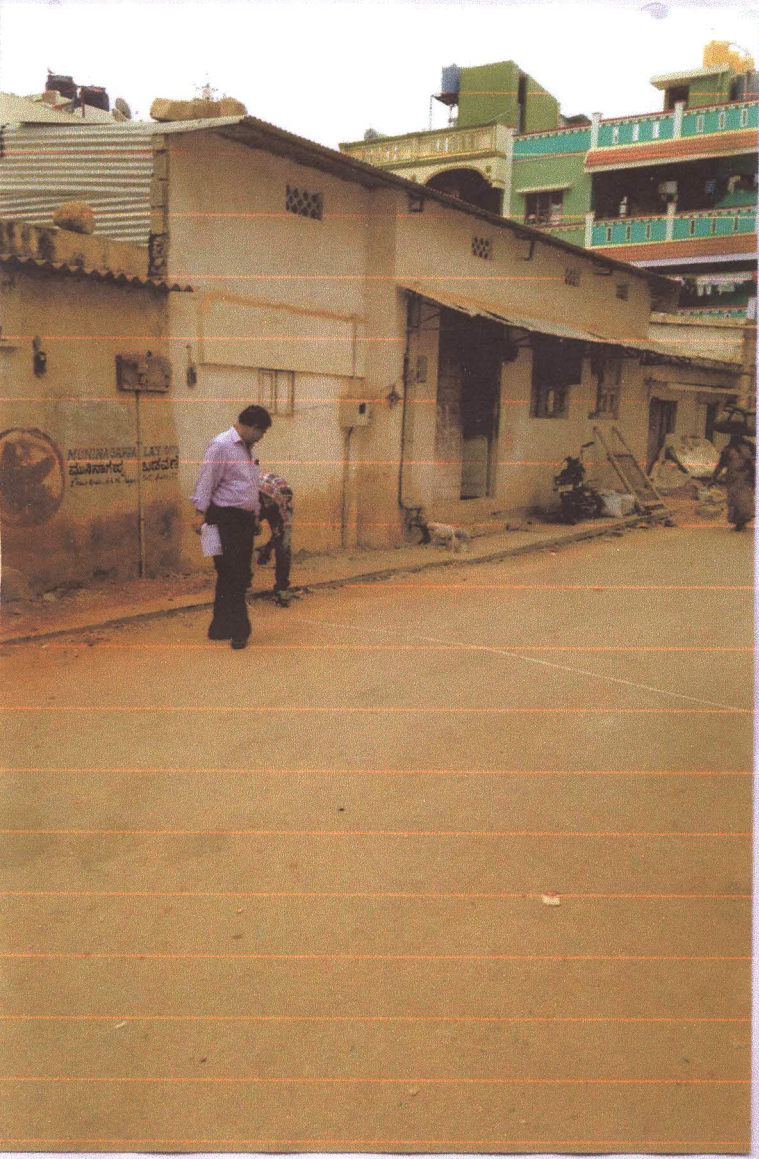

Amrutha

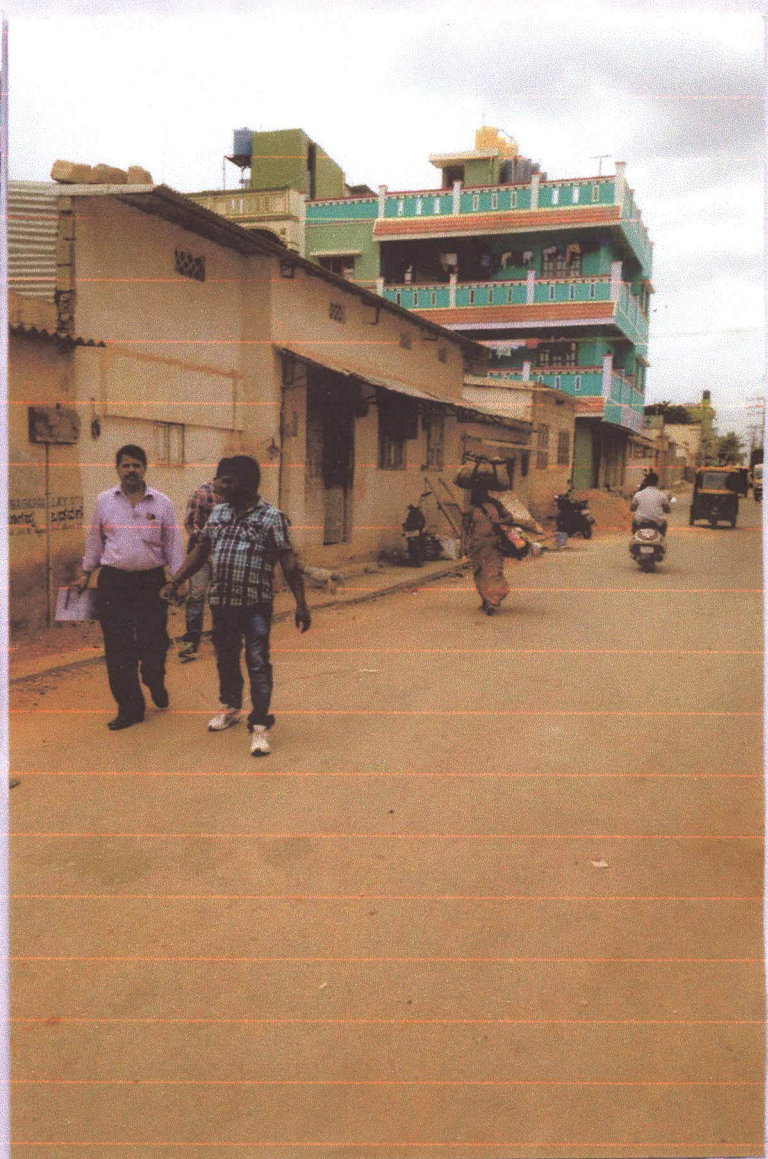

Amrutha
